PMO



BUKC – Spring 2026

Project Management Office (PMO)

Lecture # 01

PMO



Self Introduction

- Name
- Education
- Work Experience
- Motivation to join MS PM



Course Outline

- PMO- Concept Overview
- Types of PMO
- Development of a PMO- Cases
- PMO Competency Continuum
- Various Functions of PMO
- Result Based Performance Mgmt
- Best Practices
- Pit falls
- Case Studies

PMO

Project Management Office (PMO)

LEARNING OBJECTIVE

Understanding importance & frameworks to be implemented in an organization through centralization & standardization of project management practices to ensure consistency in processes, efficient resource allocations and projects alignment with strategic goals, ultimately leading to improved productivity and success ratio

What is a PMO?

Project A



Project B





PMO


Project C



Project D



What is a PMO?

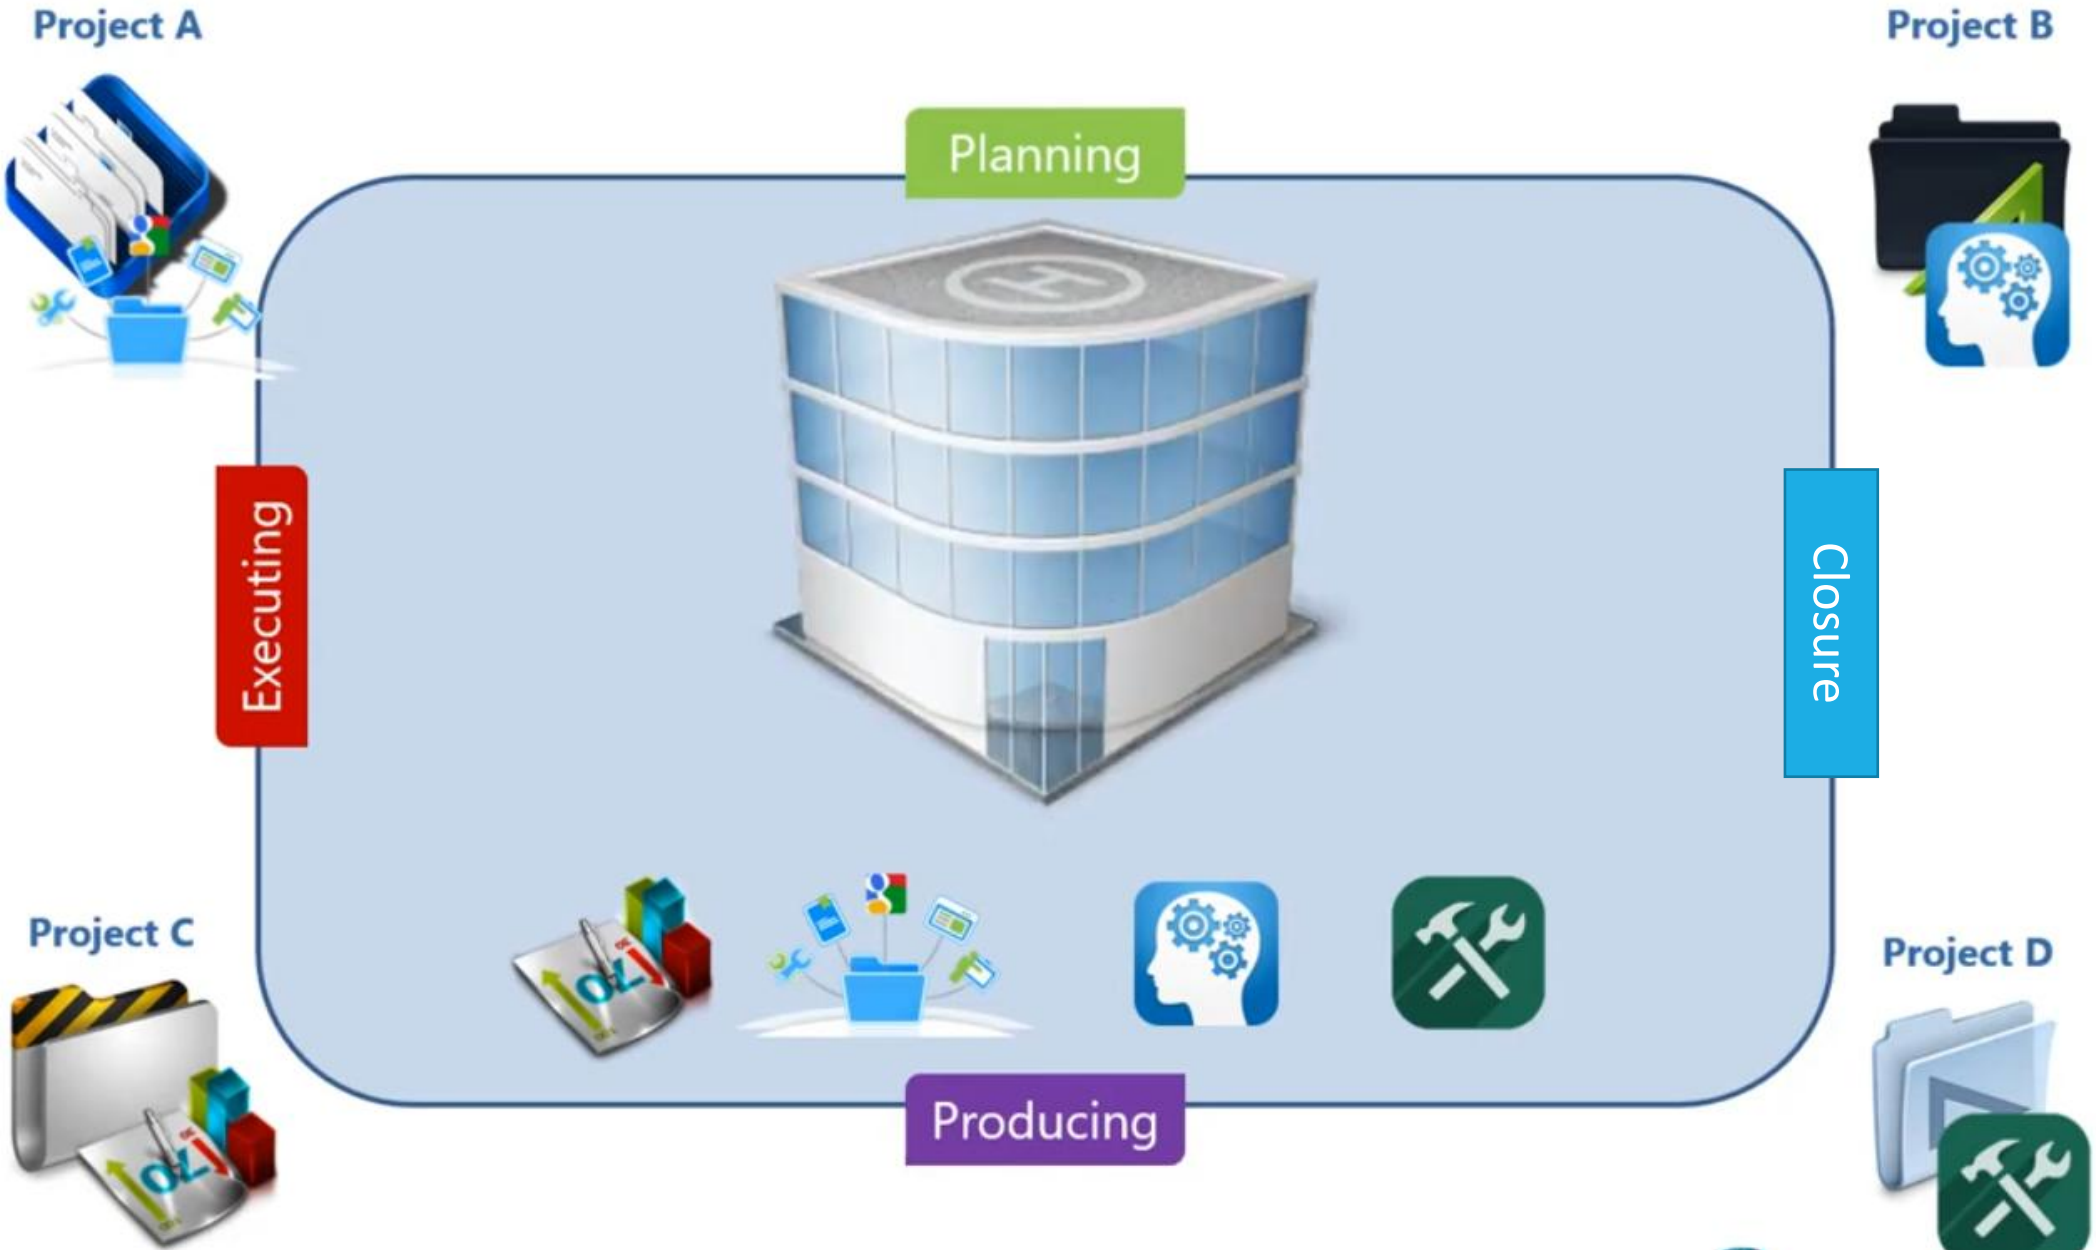
Project A
Project B
Planning
Executing
Closure
Project C
Project D
Producing


Project Management Office (PMO)

PMO

- A **Project Management Office (PMO)** is a **centralized organizational group** responsible for coordinating the project management function throughout an organization

- It **standardizes** the project-related governance processes, policies, and facilitates sharing of resources, methodologies, tools, and techniques, through a **structured approach**, to **assist** Project Managers, Project teams, functional entities and various management levels throughout the organization


- The responsibilities of a PMO can range from providing **proj mgmt support functions** to actually being responsible **to directly manage** one or more critical projects

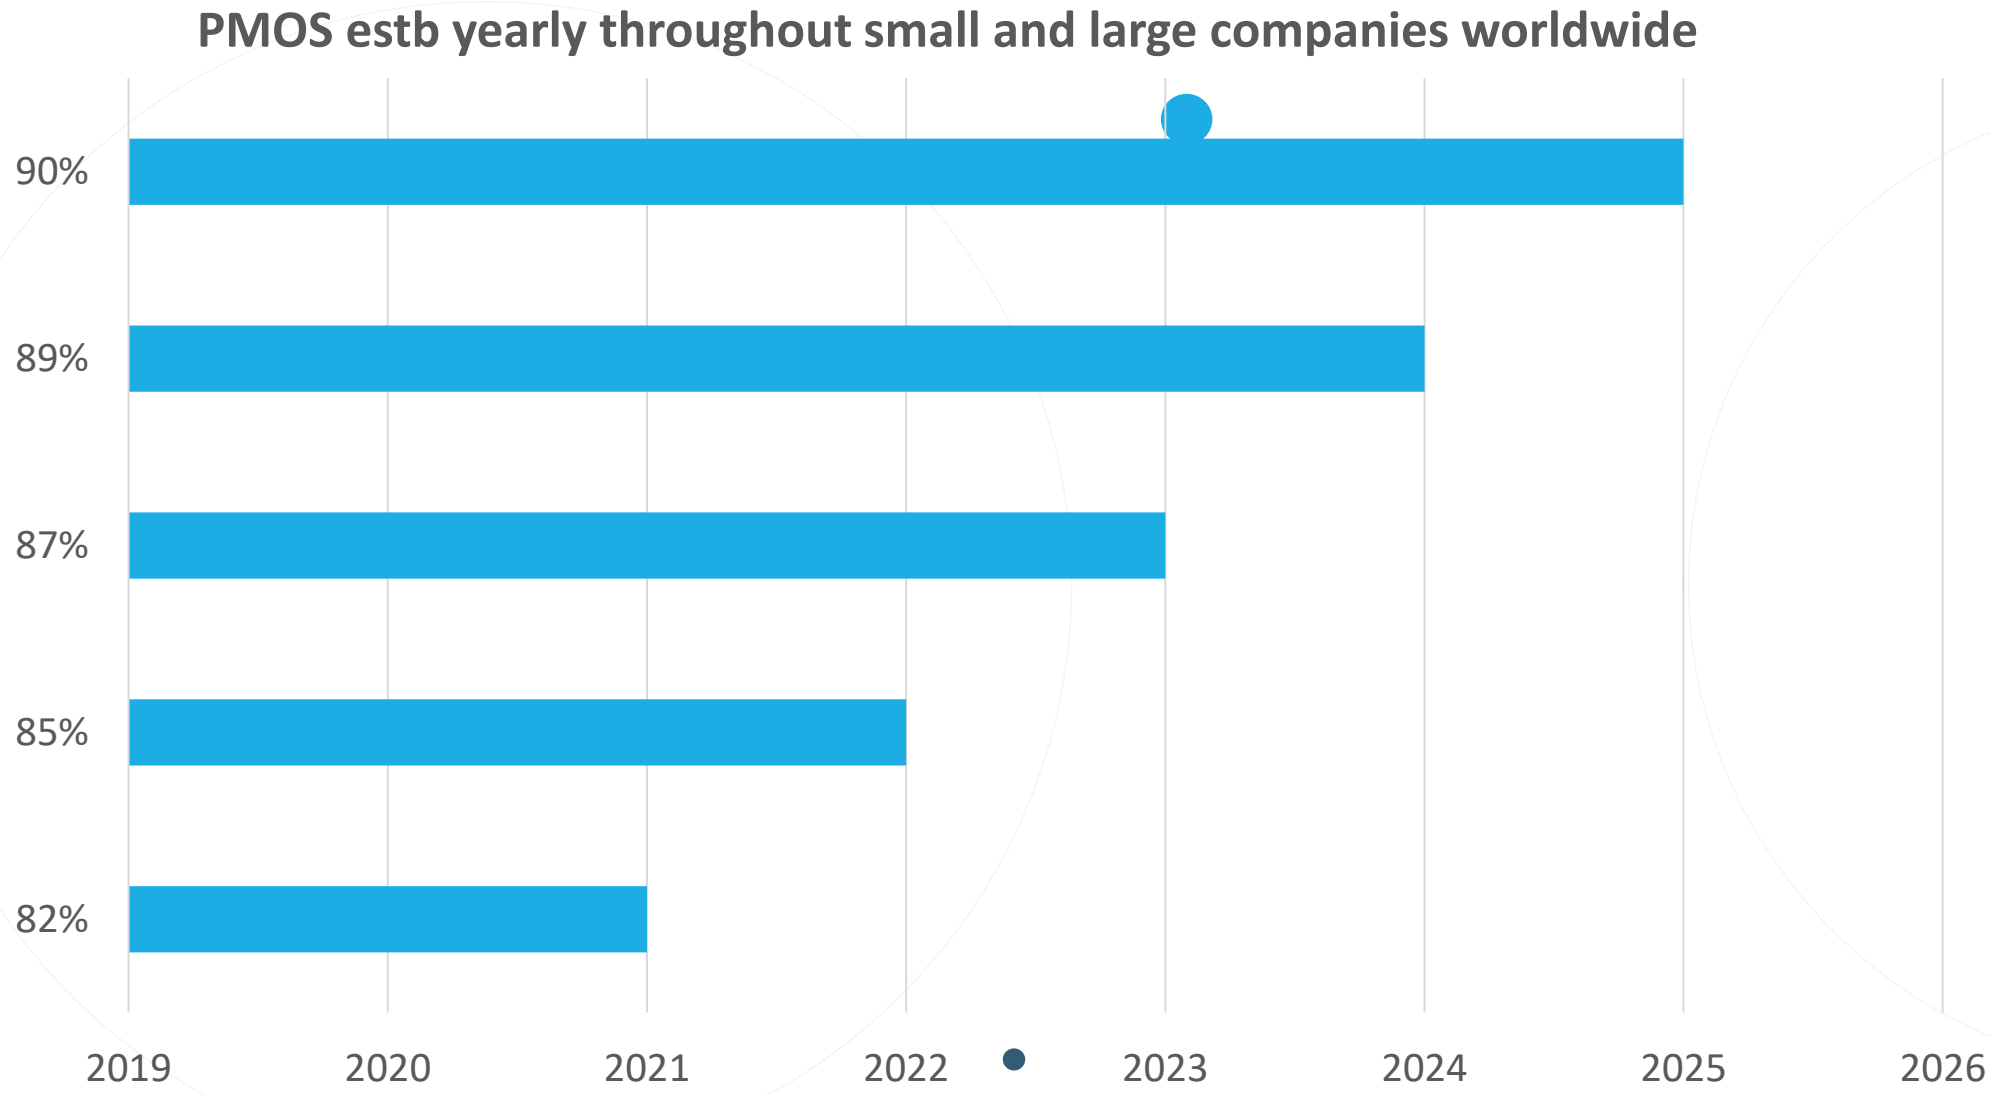

Sources: Wellingtone survey data-2025, project management statistics

Evolution of PMOs - A History

PMO

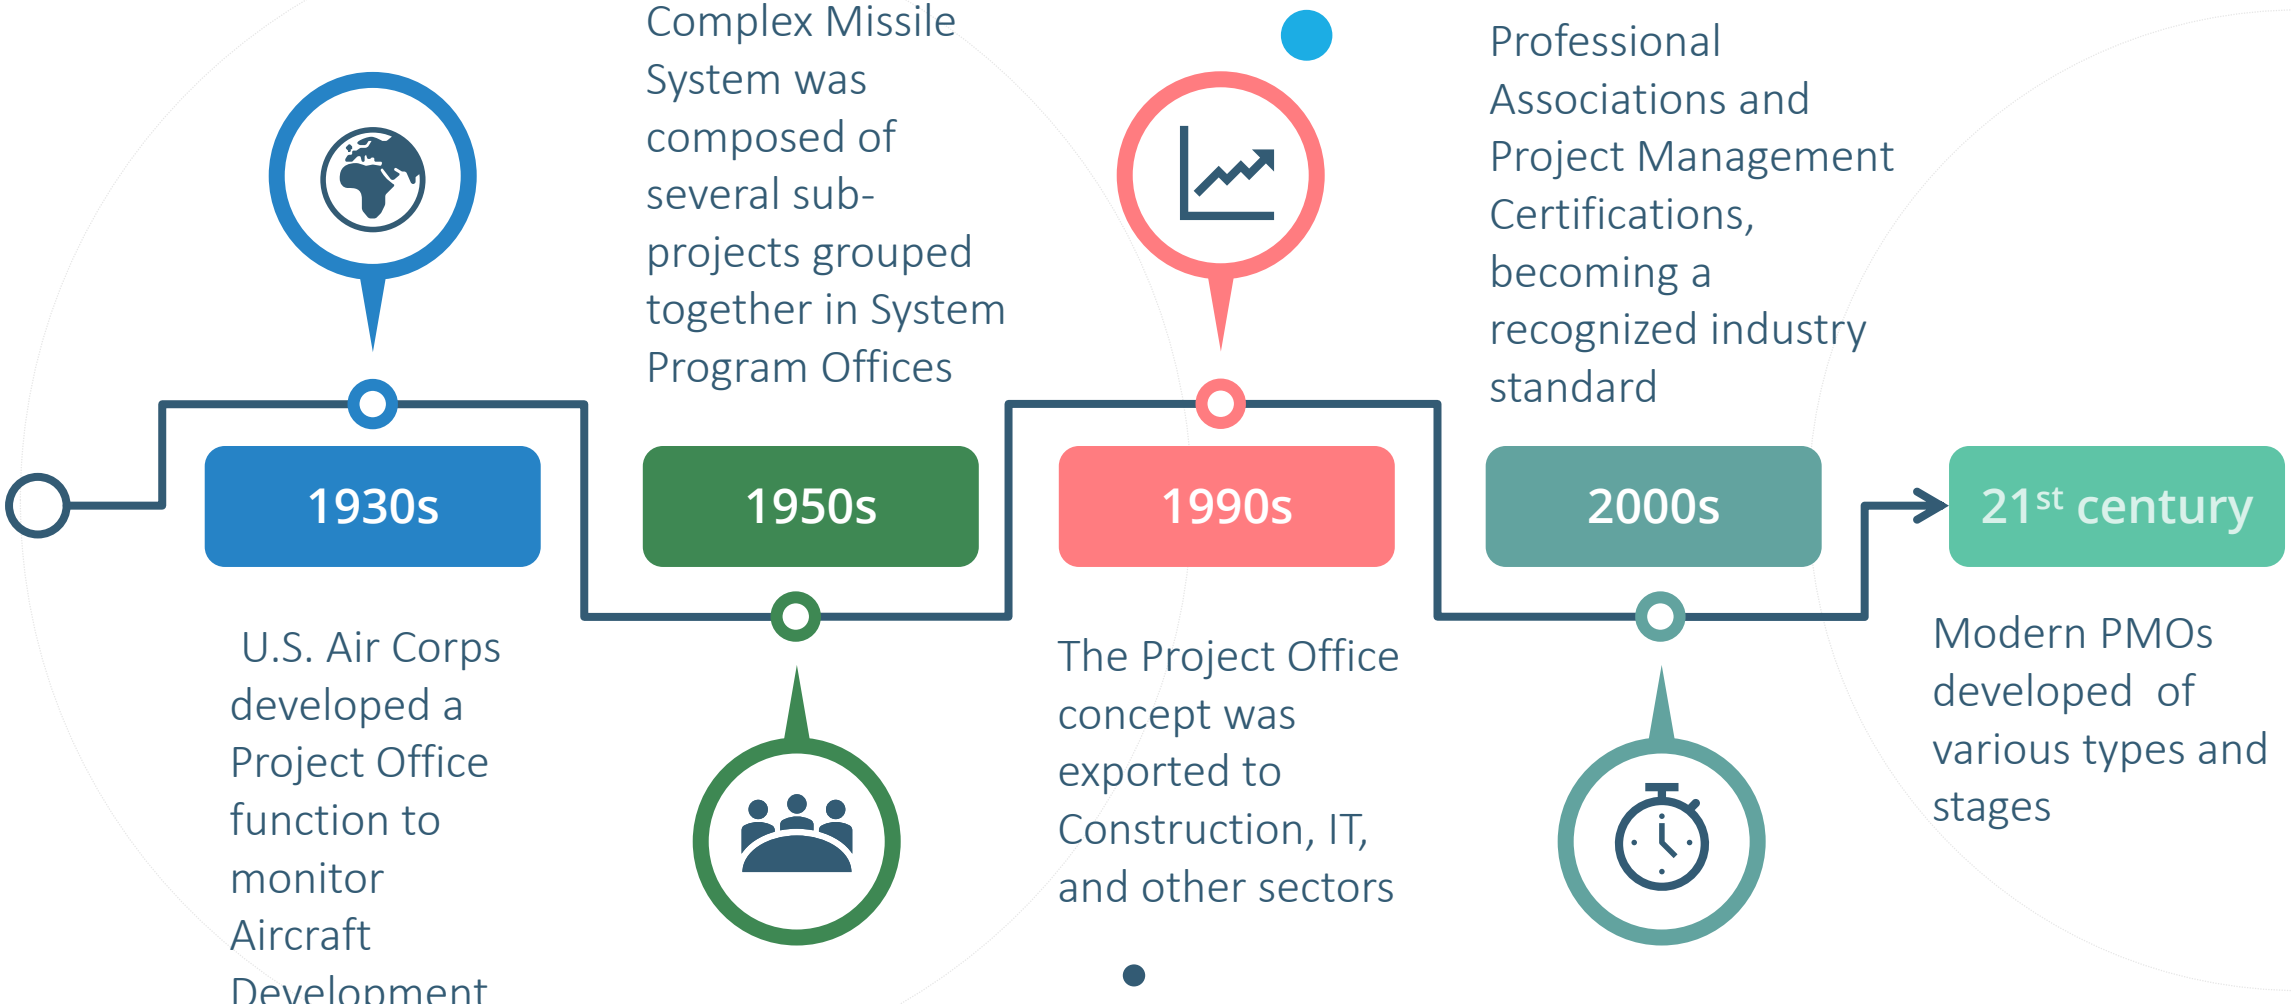


Project Management Methodology & a PMO

PMO

Proj Management Methodology function enables a **PMO** to;

- Establish the **standard approach** of proj mgmt to be used by **all Proj Managers** across the organization
- Identify & incorporate **technical** & **business processes** into the proj mgmt methodology
- Introduce proj mgmt practices **incrementally**; begin with those having the **greatest impact** on **proj** & **business success**
- Achieve **consensus/ buy-in of senior mgmt** on the desired proj mgmt approach to develop and deploy in the org, **effectively** & **efficiently**

Structure of a PMO

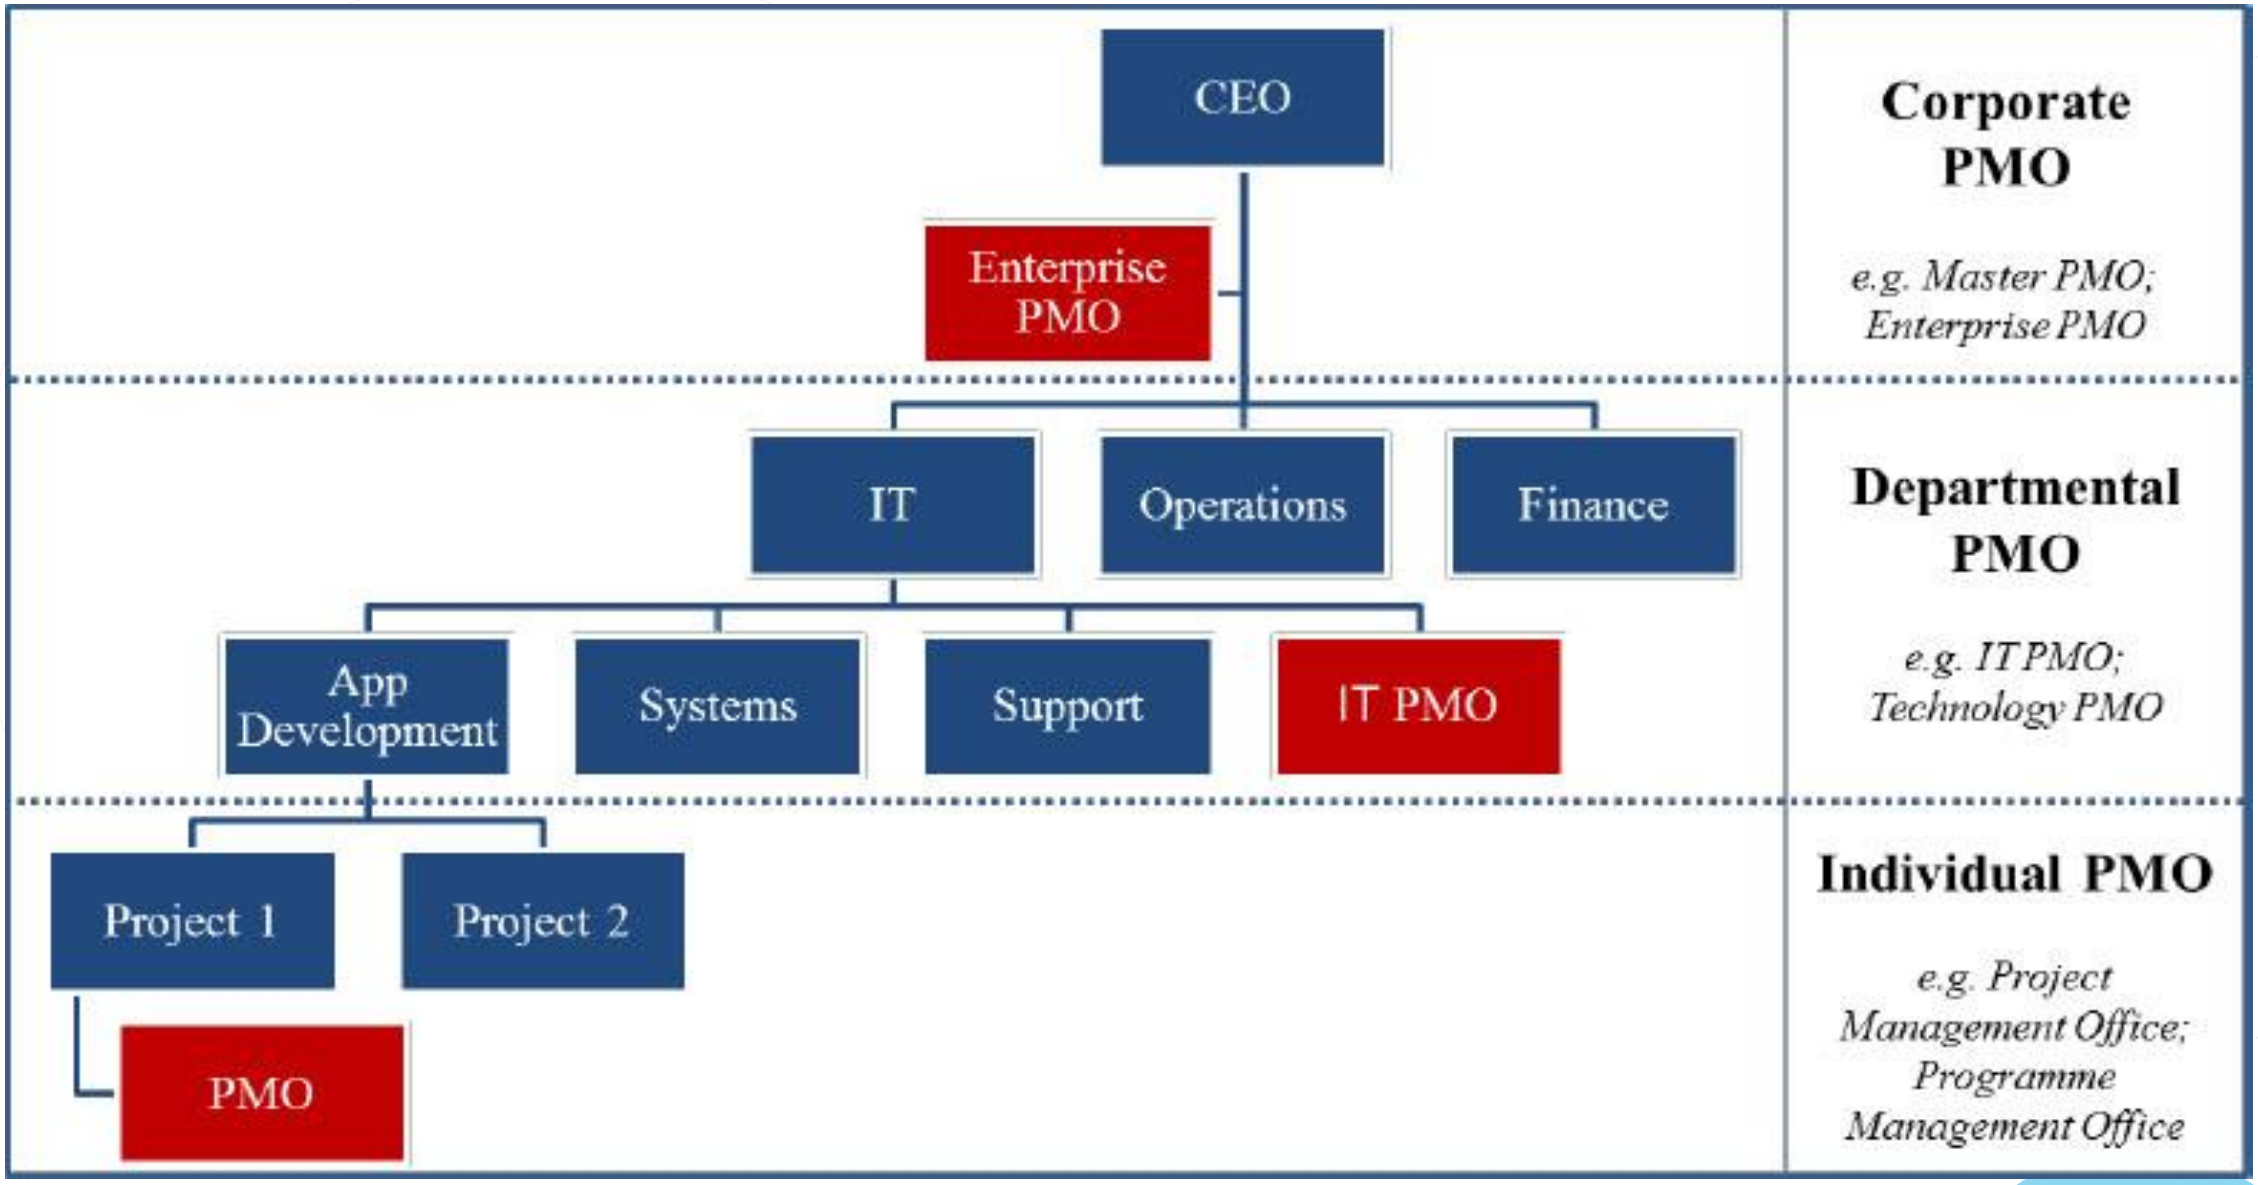

Key Roles & Responsibilities of a PMO

PMO

1. **P3 Management (Portfolio/ Program/ Project Management)**



Collaborate with leadership to align project initiatives with the overall business strategy, analyzing and prioritizing projs based on their alignment with organizational goals and **managing the overall Projects Portfolio to maximize the Return on Investment**

2. **Establishing Proj Management Methodologies**



Defining and implementing standardized proj management methodologies & processes, including **best practices, tools, and templates to ensure consistency across all organization's projs**

3. **Resource Management**





Managing the allocation of resources across all the projects within an organization, **ensuring efficient utilization of personnel, materials and budget**

Key Roles & Responsibilities of a PMO

PMO

4. **Facilitating Communication & Collaboration**

Facilitating communication & collaboration between project teams, stakeholders, and senior management is an important role **to ensure alignment, support and transparency across the organization's projects** and develop **mutual 'Trust'**



5. **Training & Development**

Delivering Proj Management Trainings to the Proj teams, **covering all or atleast important knowledge areas, to promote continuous improvement** in Proj Management skills




6. **Performance Monitoring & Reporting**

Tracking projects' progress against set Key Performance Indicators, analysis & evaluation, identification of potential risks, areas of improvement, suggesting timely way forward to the project office as well as providing recommendations to top management for decision making



Types of PMO

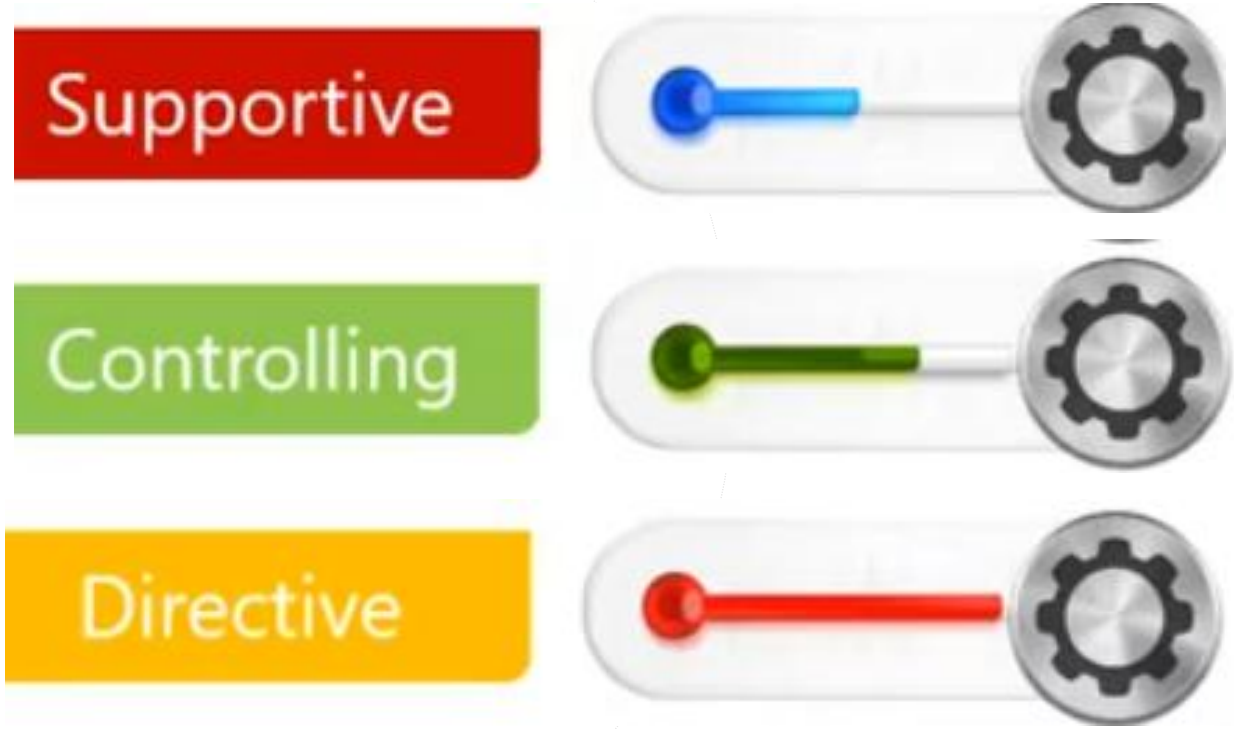


Types of PMO - Supportive

PMO

- **Consultative role**
- Acts as a **Repository** for the organization's projects
- Provides **templates**, **best practices** and **training**
- Records and keep track of **lessons learned**
- **Very low degree of control** in projects



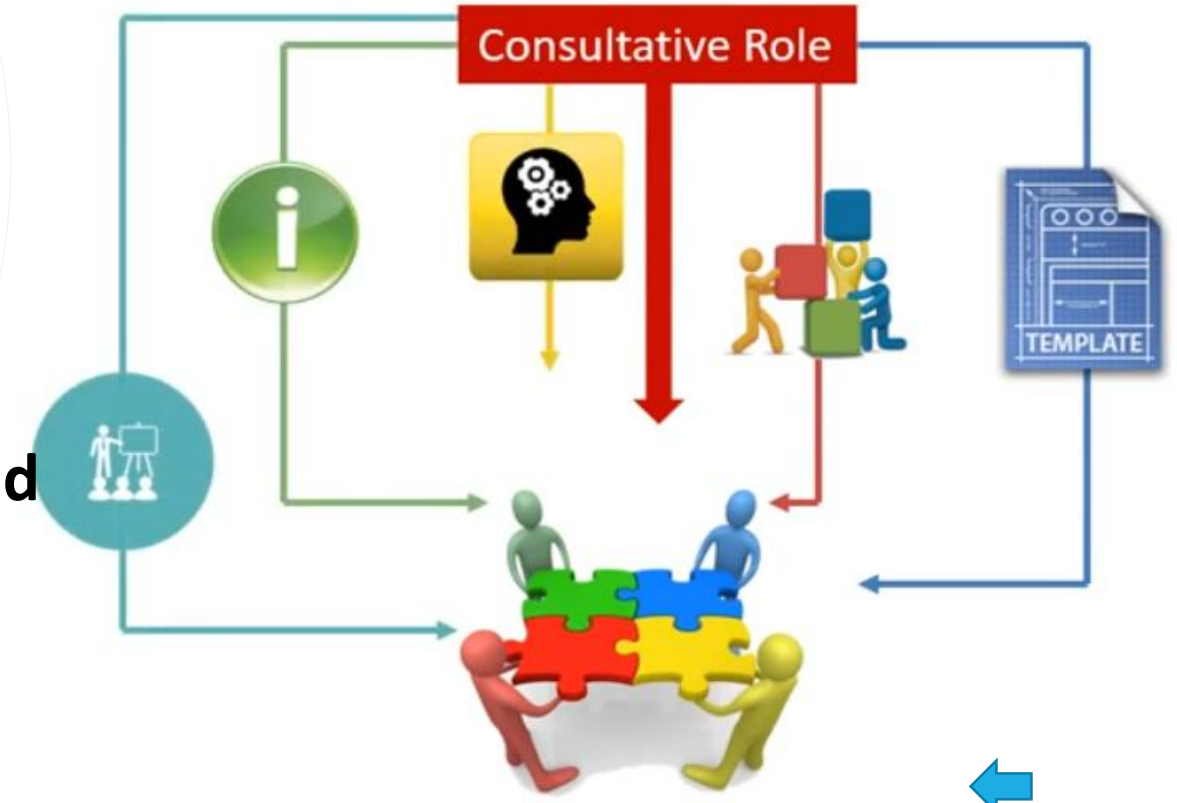

Types of PMO - Supportive

PMO

- **Consultative role**
- Acts as a **R**
  organizatio
- Provides **te**
  training
- Records and keep track of **lessons learned**
- **Very low degree of control** in projects




Low Degree of Control



Types of PMO - Controlling

PMO

- Provides **support** and **guidance** to projects through best practices & lessons learned
- **Designs** and **establishes** policies, processes, procedures and tools to be implemented
- **Check/ Verify** whether **standardized or approved** Proj Management artifacts are applied in the projects
- **Enforces compliance** to approved practices
- **Moderate degree of control** in projects

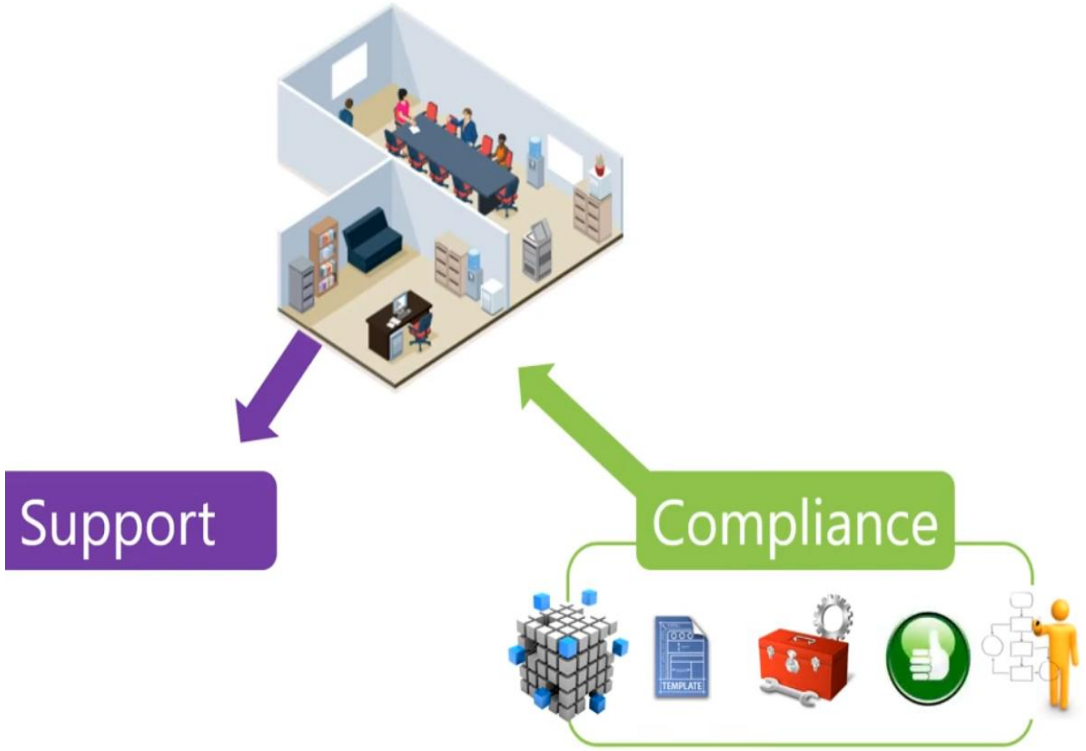

Types of PMO - Controlling



Moderate Degree of Control

Types of PMO - Directive

PMO

- **Directly manages** the projects
- Ensures **alignment** to the organizational strategy and short to long term goals
- Has autonomy to **make decisions** on organizations' portfolio of projs, by keeping top mgmt onboard
- Proj Managers can be **assigned by** and **report** to this PMO
- **High degree of control** in the projects



Types of PMO - Directive

PMO

- **Directly manages** the project(s)
- Ensures **alignment** to the organizational strategy and
- Has autono projects
- Proj Managers are **assigned by** and **report** to this PMO
- **High degree of control** in the projects



High Degree of Control

Importance of PMO in Organizations

- As the technical & business world grows increasingly complex, and projects become more integral to an organization's success, **the need for a structured approach to manage projects is paramount**
- A well-functioning PMO not only streamlines project management processes but also **ensures alignment with the strategic goals of the organization**

Importance of PMO in Organizations

- **Business Integrator** – centralizing proj management tasks in a PMO gives advantage of **specialization, experience** and **expertise of PMO HR, consistency in practices and processes** leading to **predictable results**

- **Business Unit** – better visibility, stakeholders' confidence, efficient resource allocation, less wastage, improved productivity and ROI, thus **better control over projects**

Quick Assessment

PMO

1. Establishes and enforces project management standards (C)
2. Coordinates some or all projects in an organization (S)
3. Appoints and directs Project Managers (D)
4. It provides frameworks and resources to help Proj Mgrs succeed but doesn't expect compliance (S)
5. It prioritizes projects and their funding (D)
6. PMO audits the project status at regular intervals to ensure reporting integrity (C)
7. Recommends common templates, processes, and procedures to be used on projects to promote consistency and streamlining efforts throughout the organization (S)
8. Has the highest level of control over the projects (D)
